
## **TENTH AVENUE MARINE TERMINAL MODERNIZATION PROJECT - TIGER**



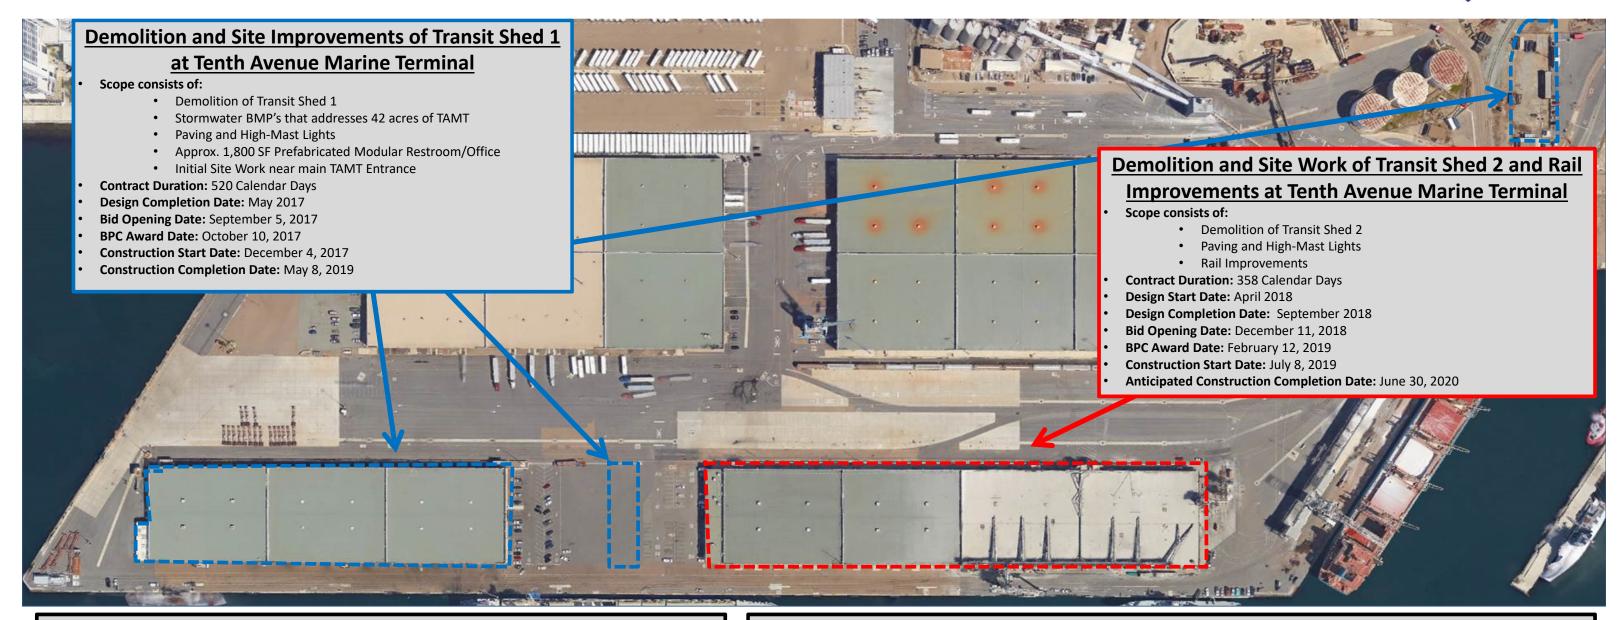

KEY MILESTONE DATES		
Milestone	Date	
Grant Award	October 26, 2015	
NEPA / EIR Completion	November 16, 2016	
Grant Execution	January 10, 2017	
Obligation of Funds	September 12, 2017	
Overall Construction Completion (Projected)	June 30, 2020	
Period of Performance Completion (Projected)	October 1, 2020	
Project Close-Out Date (Projected)	December 1, 2020	
Funds Expiration	September 30, 2022	

OVERALL PROJECT BUDGET		
Funding Source	Cost	Scope of Work
Port of San Diego	\$14,000,000	50% of Demo, Pavement, Utilities + Design, Modular Facilities
MARAD	\$10,000,000	50% of Demo, Pavement, Utilities
TOTAL	\$24,000,000	
